Movement Quest project progress

Who handled what

Emmanuel's planned work was the screens, buttons, forms, workout flow, settings, and documents. Marcus's planned work was saving data, workout suggestions, testing, and APK checks.

We use ClickUp to track tasks and GitHub to keep the code.

Project board | GitHub repository

How the board works

Tasks move from Backlog → Ready → In progress → Review/Test → Done.

Each person should have one task in progress. No more than two tasks should be waiting for review. A coding task is Done after it works, passes its checks, gets reviewed, and is merged.

What got done

MQ05: Added the five-screen navigation and reusable plan cards. Three tests passed. Marcus approved PR #1 on October 31 at 1:15 PM EDT, but it hasn't been merged. 6edc425.

MQ06 and MQ09: Added saved plans, saved sets, and workout session counts. Marcus shared his code in a folder on October 28. That code was connected to the app and adjusted to match the project. PR #2 records 43 passing tests. The folder was shared outside GitHub, so the commits don't show all the original work. d78cc83, adec1a6, abcac51.

MQ10 and MQ11: Added workout controls, history changes, and saved settings. These were later connected to the database. b3a550d.

MQ12: Added workout suggestions based on equipment and the last finished workout. Users can see the reason, open the plan, or skip it. PR #3 records 53 passing tests and no analysis issues. 9e1f6f6.

MQ14 and MQ15: Checked offline saving on two emulators and tested the suggestions. Both suggestion methods picked the expected plan in three out of four valid examples. f268bbf, 016a826.

One example from task to test

MQ09 asks the app to save sets under the right plan and count a finished workout once.

The database code handles saving and grouping the sets. Tests check the saved records and how the screens use them.

On both emulators, saved data stayed after reopening the app. Repeated taps didn't create duplicates. The app also blocked deleting a plan that still had saved sets.

Database code | Database tests | Screen tests | Offline results

Board pictures


The October 18 picture shows 15 tasks in Backlog, 3 Ready, and 1 In progress.

The October 31 board shows 8 Done, 5 Review/Test, 1 In progress, and 5 Backlog.


Current review status

Marcus approved PR #1. PRs #1, #2, and #3 are still open and haven't been merged.

October 18 board

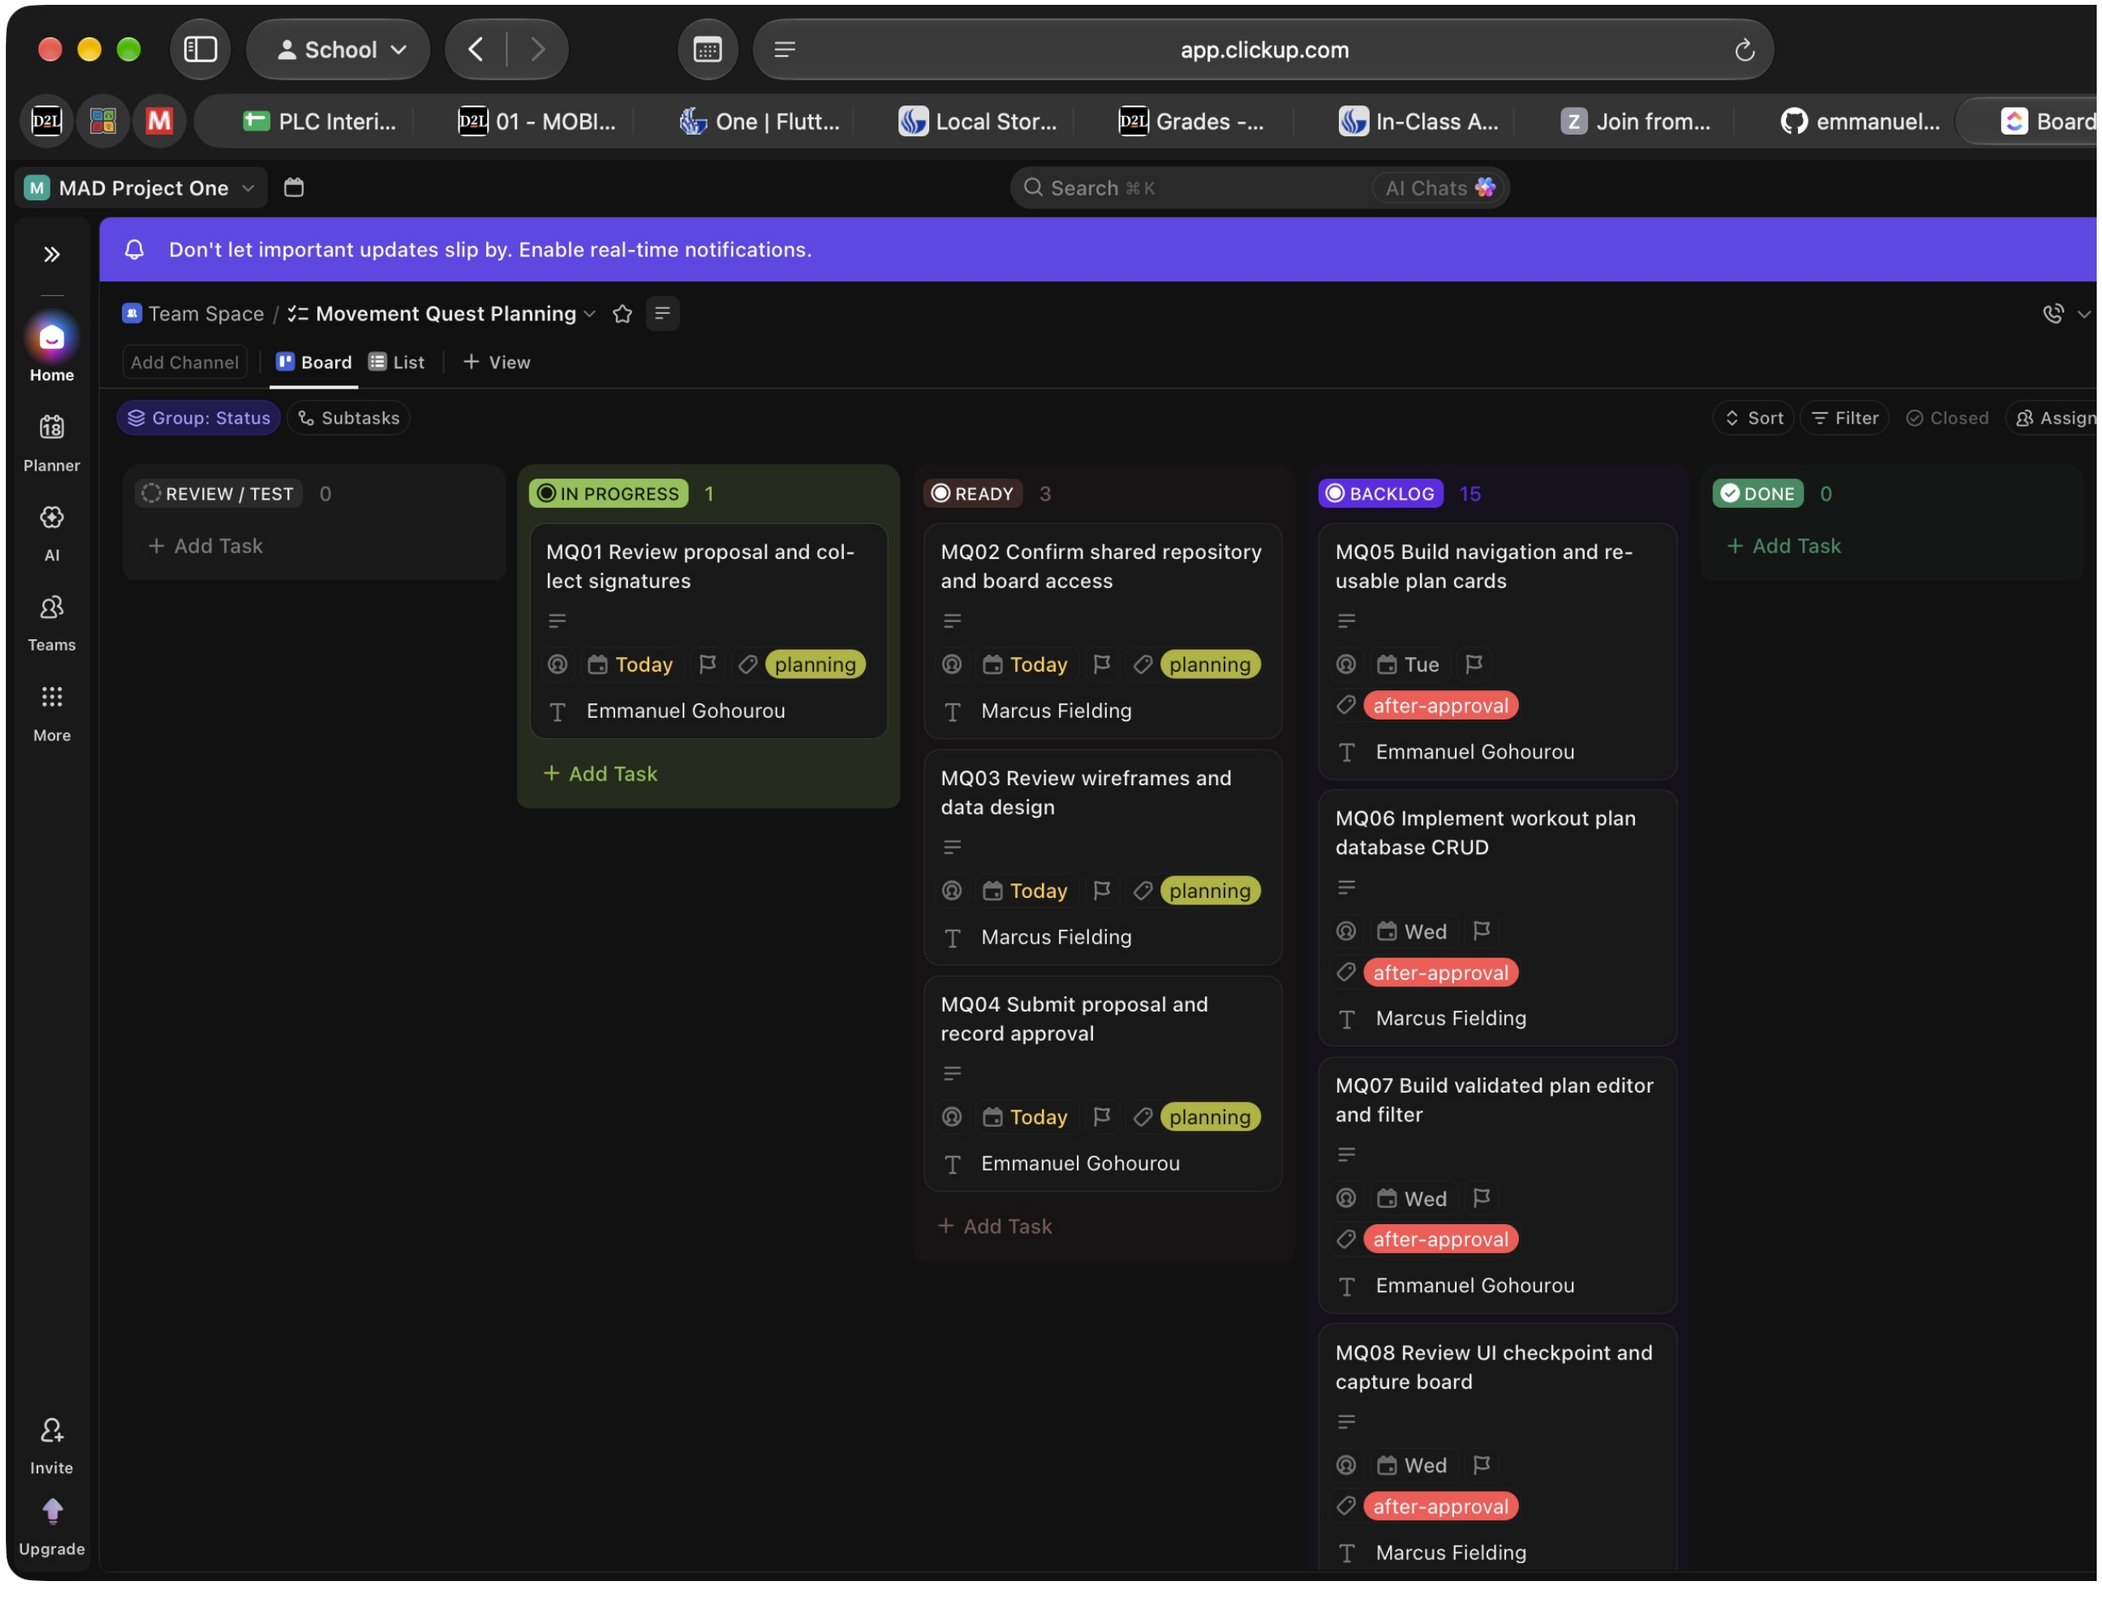

October 31 board

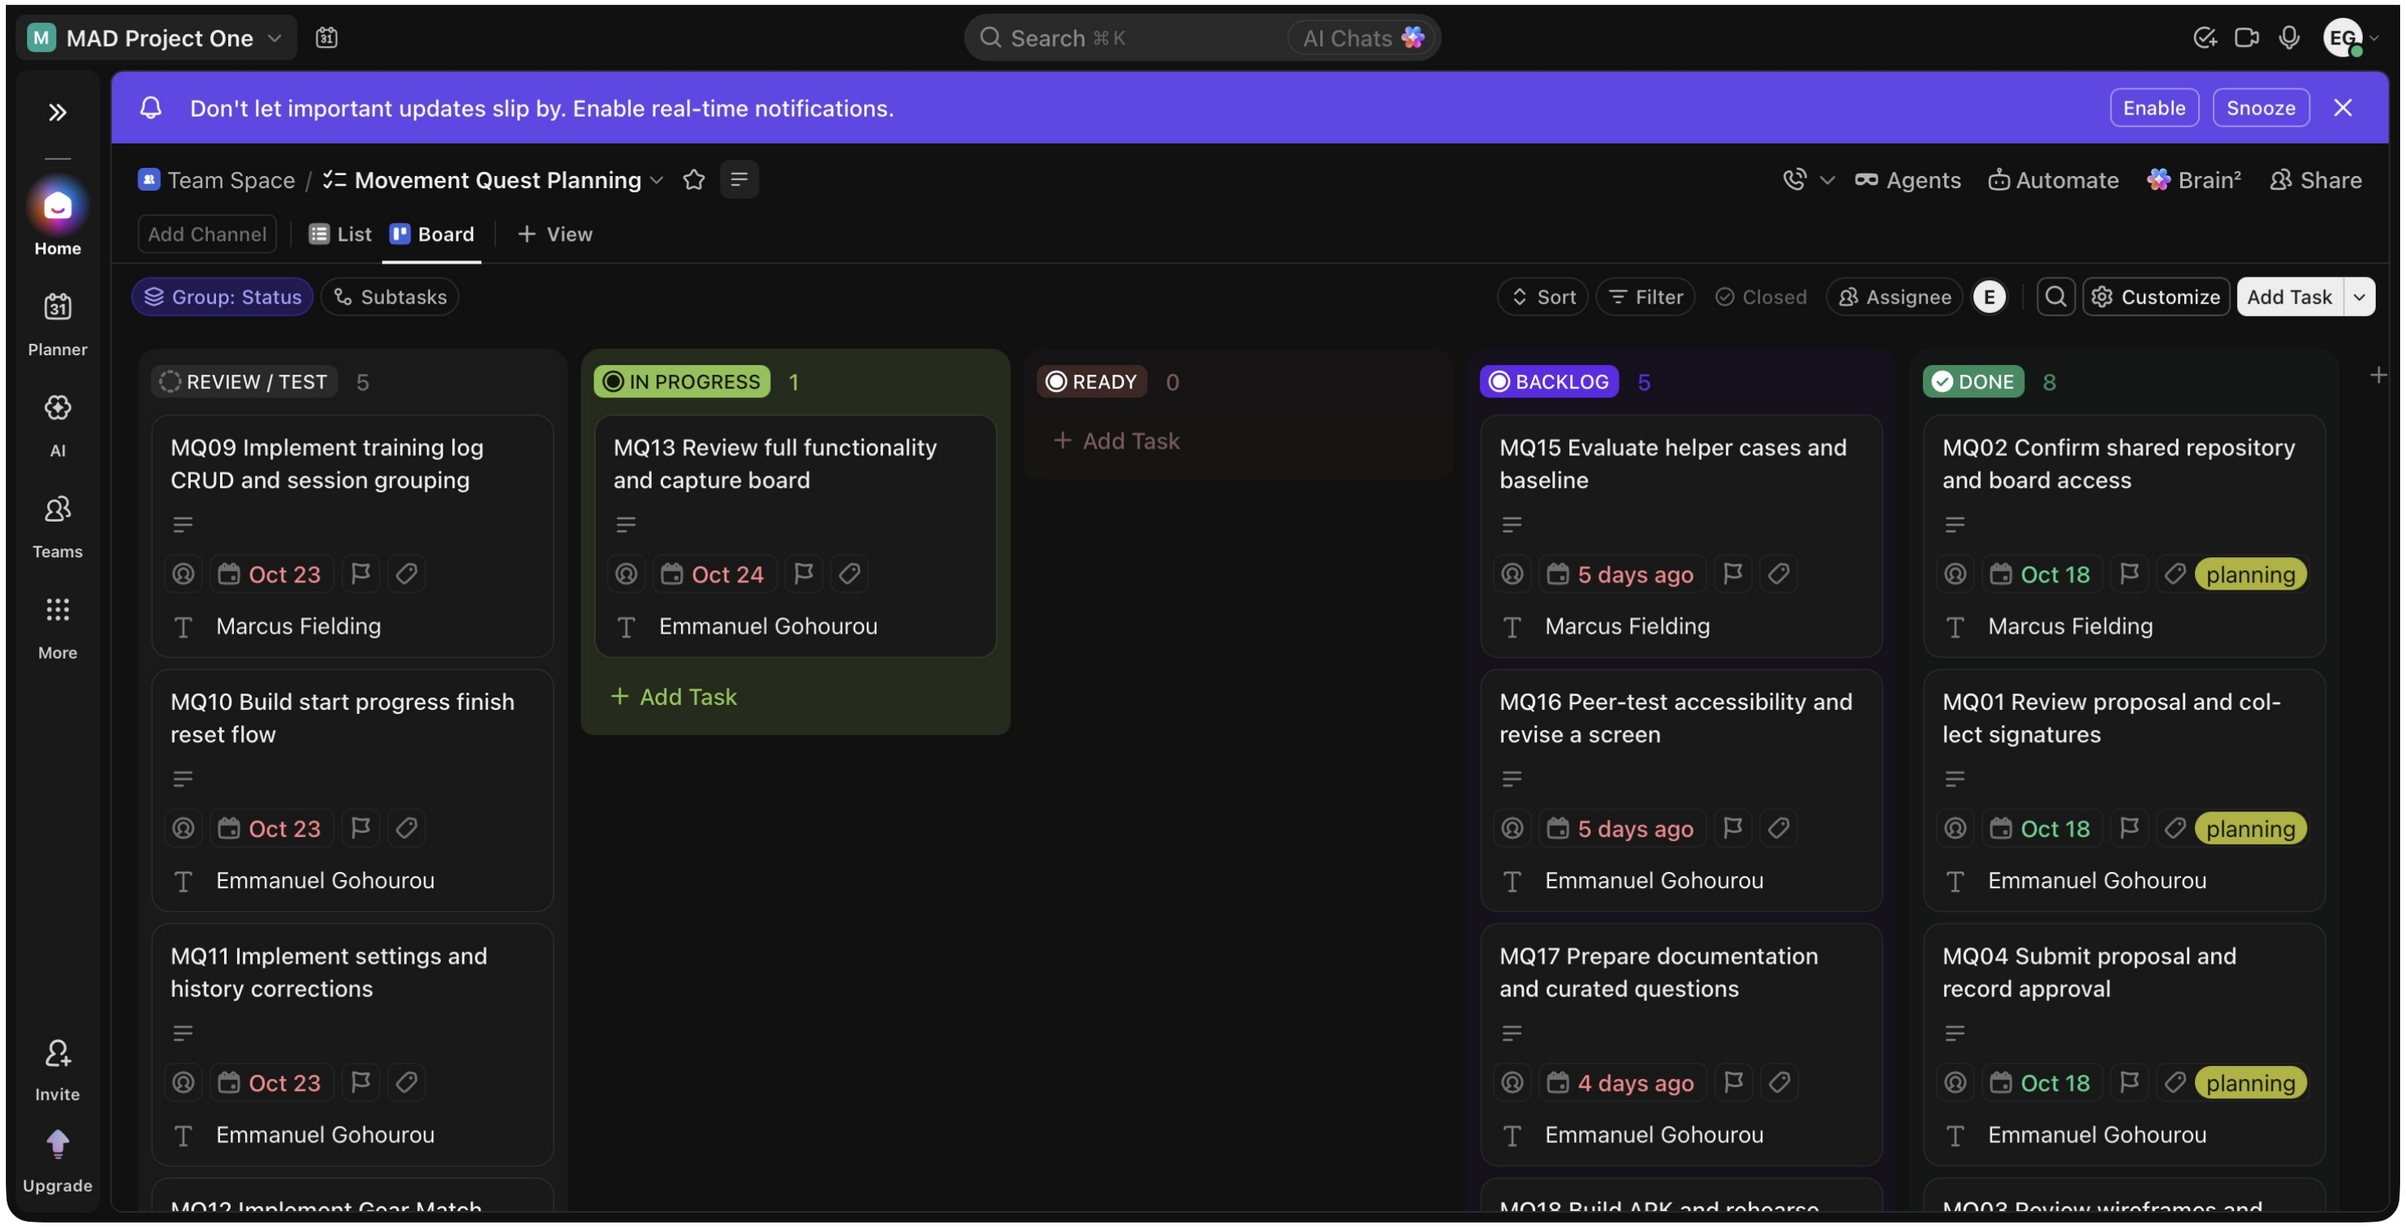

October 31 board lower view

